



## General Manager's Report Item 12:

Status Report on Cal-Am Compliance  
with SWRCB Orders and Seaside Basin  
Decision as of May 1, 2016

*Meeting Date: May 16, 2016*

*Staff contact: David J. Stoldt*

# Actual versus Target Production for Cal-Am: Oct to Apr 2016 (All Values in Acre-Feet)

## Production vs. CDO and Adjudication to Date: WY 2016

(All values in Acre-Feet)								
Year-to-Date Values	Carmel River Basin <sup>2</sup>	Seaside Groundwater Basin		Water Rights and Projects <sup>7</sup>			MPWRS Total	Percent Below Target
		Coastal	Laguna Seca	ASR Recovery	Table 13	Sand City <sup>3</sup>		
Target	4,576	1,100	22	0	211	175	6,084	<b>8.7%</b>
Actual <sup>4</sup>	4,638	762	153	0	137	61	5,553	
Difference	-62	338	-131	0	75	114	531	

### Notes:

1. “Sand City” refers to the Sand City Desalination Facility, which pumps brackish water from the Seaside Groundwater Basin as source water. The Sand City values refer to yield from the facility.
2. “Carmel River Basin” production includes withdrawals for injection to the Aquifer Storage and Recovery (ASR) Project.
3. “MPWRS” refers to Monterey Peninsula Water Resource System.
4. Carmel River Basin Target reflects assumed annual production of 300 AF from Sand City.
5. Production numbers are estimated pending finalization of CAW production data.
6. Carmel River Basin target represents quarterly adjustments based on differences between budgeted values and actual production from other sources.
7. Table 13, ASR Recovery, and Sand City Production are not counted in MPWRS production.



# Production for Customer Service for Cal-Am: Oct to Apr 2016 (All Values in Acre-Feet)


## Monthly Production from all Sources for Customer Service: WY 2016

(All values in Acre-Feet)						
	<b>Carmel River</b>	<b>Seaside Basin</b>	<b>ASR Recovery</b>	<b>Table 13</b>	<b>Sand City</b>	<b>Total</b>
Oct-15	568	288	0	0	11	867
Nov-15	479	187	0	0	0	666
Dec-15	527	117	0	0	0	644
Jan-16	495	87	0	42	2	627
Feb-16	606	44	0	10	5	664
Mar-16	427	139	0	81	15	662
Apr-16	701	54	0	3	28	786
May-16						
Jun-16						
Jul-16						
Aug-16						
Sep-16						
<b>Total</b>	<b>3,803</b>	<b>915</b>	<b>0</b>	<b>137</b>	<b>61</b>	<b>4,915</b>

### Notes:

1. “Sand City” refers to the Sand City Desalination Facility, which pumps brackish water from the Seaside Groundwater Basin as source water. The Sand City values refer to yield from the facility.
2. “ASR Recovery” refers to the amount of water recovered for customer service from the Aquifer Storage and Recovery (ASR) Project .
3. “Table 13” refers to water diverted and consumed under Table 13 Water Rights within the Carmel River Basin when river flows are in excess of permit limits.
4. Carmel River Basin Target reflects assumed annual production of 300 AF from Sand City.
5. Production numbers are estimated pending finalization of CAW production data.

# Recorded Rainfall at San Clemente Dam: Water Year 2016

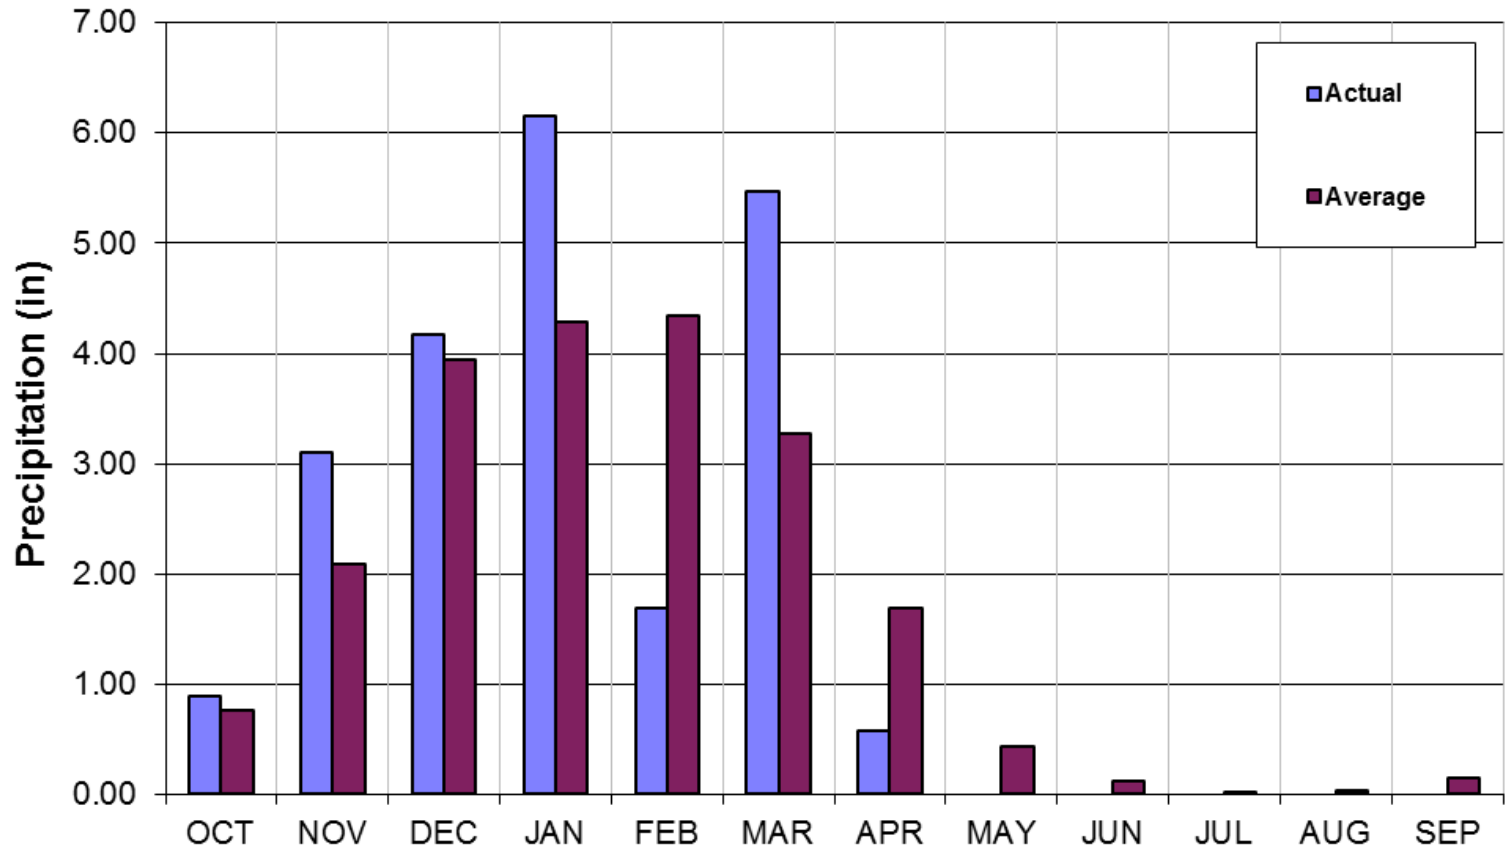

# Estimated Unimpaired Carmel River Flow at San Clemente Dam: Water Year 2016

